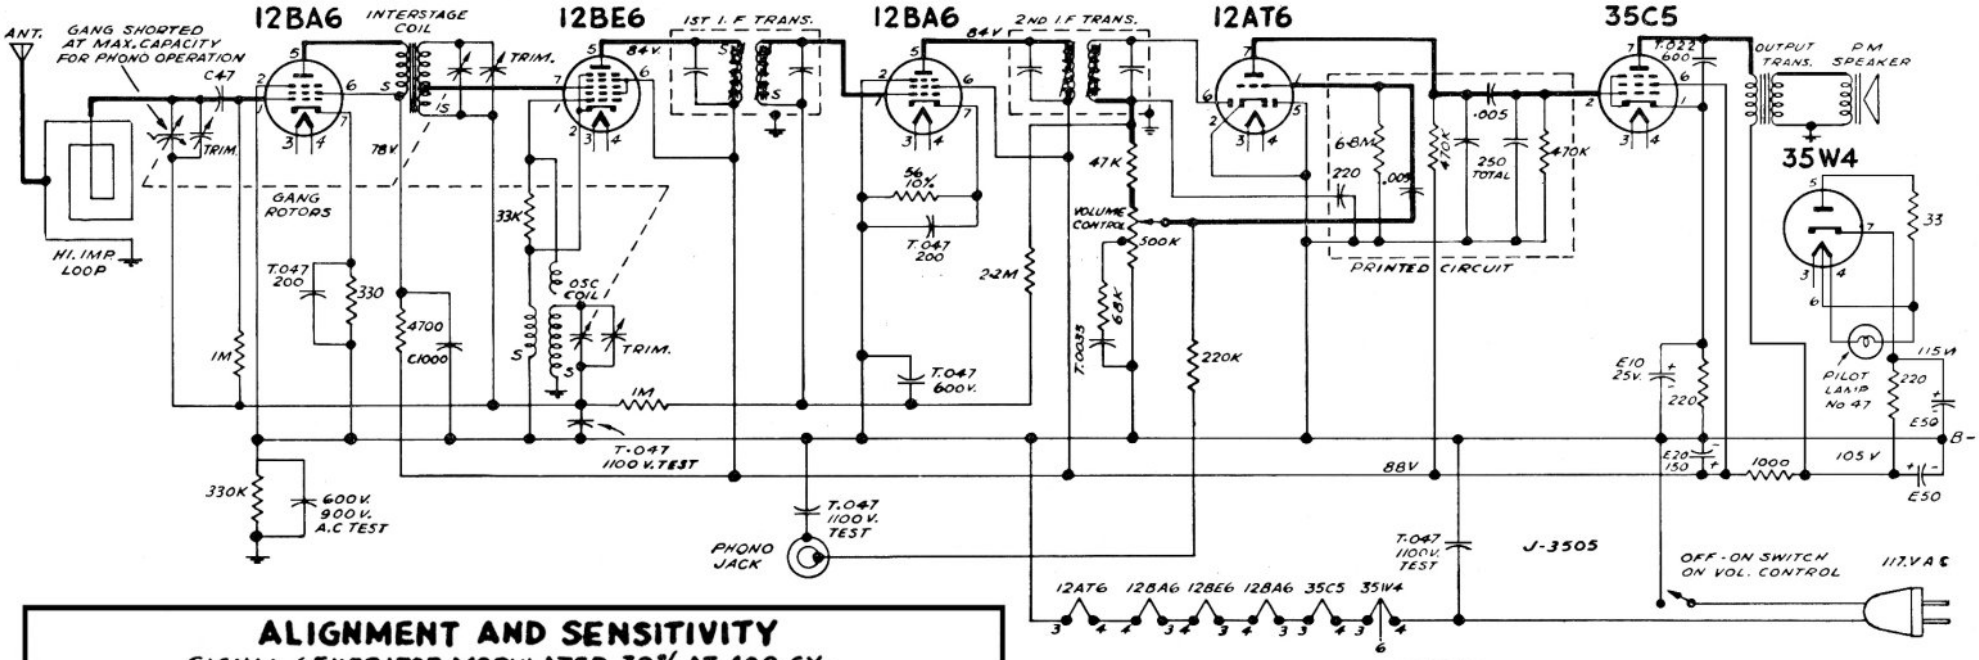

ALIGNMENT AND SENSITIVITY

SIGNAL GENERATOR MODULATED 30% AT 400 CY.

STEP	APPLY SIGNAL AT KC.	APPLY SIGNAL TO	THRU SERIES DUMMY	SET GANG AT	ADJUST FOR MAX. OUTPUT	NOMINAL SENSITIVITY FOR 50 MILLIWATTS OUTPUT
1	455	12BA6 I.F. #1 PIN	.05	—	2ND. I.F.	2000
2	455	12BE6 #7 PIN	.05	MINIMUM CAPACITY	1ST. I.F. 2ND. I.F.	65
3	1460	12BA6 #1 PIN	.05	1460 KC.	OSC. AND INTERSTAGE TRIMMERS	
4	1460	ANT.	*	1460 KC	ANTENNA & INTERSTAGE TRIMMER	10 μv/M.
5	600	ANT.	*	600 KC.	CHECK ONLY	30 μv/M.

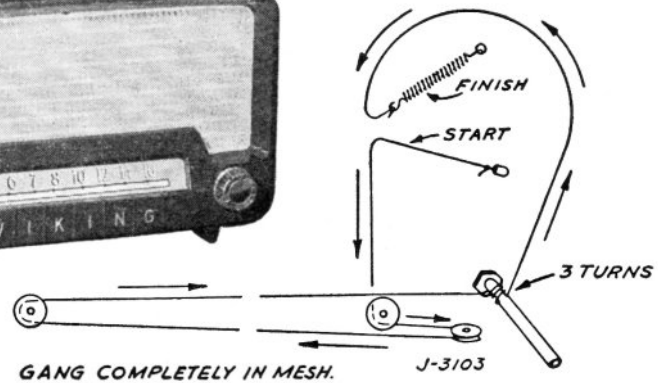

VIKING RM-201, RM-221, RM-221AR, RM-274
